

Application and Certificate for Payment

TO OWNER: STFP District No. 1
522 Robert Boulevard
Slidell, LA 70458

PROJECT:
STFD New Training Facility
34780 S. Range Road
Slidell, LA 70460

APPLICATION NO: 4

PERIOD TO: 10/31/25

CONTRACT FOR: St. Tammany Fire Protection Dis

CONTRACT DATE:

PROJECT NOS: 2507

Distribution to:

OWNER

ARCHITECT

CONTRACTOR

FIELD

OTHER

FROM CONTRACTOR:
M Natal Contractor, Inc.
P.O. Box 518
Slidell, LA 70459

VIA ARCHITECT:

CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for payment, as shown below, in connection with the Contract.
Continuation Sheet, AIA Document G703, is attached.

1. ORIGINAL CONTRACT SUM	\$	458,520.00
2. Net change by Change Orders	\$	0.00
3. CONTRACT SUM TO DATE (Line 1 +/- 2)	\$	458,520.00
4. TOTAL COMPLETED & STORED TO DATE (Column G on G703)	\$	341,980.44
5. RETAINAGE:		
a. 10.0 % of Completed Work (Column D + E) on G703	\$	33,768.04
b. 10.0 % of Stored Material (Column F on G703)	\$	430.00
Total Retainage (Lines 5a + 5b or Total in Column I of G703)	\$	34,198.04
6. TOTAL EARNED LESS RETAINAGE	\$	307,782.40
(Line 4 less Line 5 Total)		
7. LESS PREVIOUS CERTIFICATES FOR PAYMENT	\$	253,479.13
(Line 6 from prior Certificate)		
8. CURRENT PAYMENT DUE	\$	54,303.27
9. BALANCE TO FINISH, INCLUDING RETAINAGE (Line 3 less Line 6)	\$	150,737.60

CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous months by Owner	\$ 0.00	\$ 0.00
Total approved this Month	\$ 0.00	\$ 0.00
TOTALS	\$ 0.00	\$ 0.00
NET CHANGES by Change Order	\$	0.00

The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous Certificates for Payment were issued and payments received from the Owner, and that current payment shown herein is now due.

CONTRACTOR:

By: [Signature]

Date: 10-23-25


State of: Louisiana

County of: St. Tammany Parish

Subscribed and sworn to before me this 23 day of October 25

Notary Public: [Signature]

My Commission expires: At Death

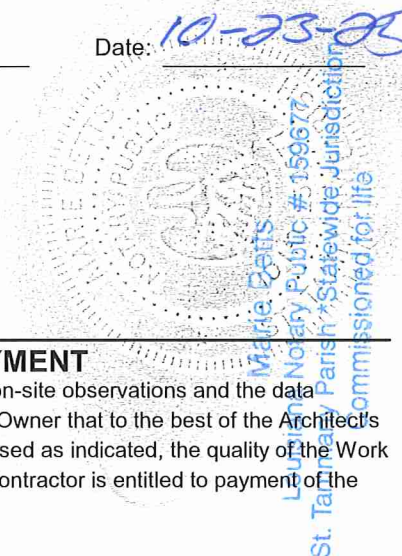

ARCHITECT'S CERTIFICATE FOR PAYMENT

In accordance with the Contract Documents, based on on-site observations and the data comprising this application, the Architect certifies to the Owner that to the best of the Architect's knowledge, information and belief the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.

AMOUNT CERTIFIED

(Attach explanation if amount certified differs from the amount applied. Initial all figures on this Application and on the Continuation Sheet that are changed to conform with the amount certified.)

ARCHITECT:

By: _____

Date: _____

This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are without prejudice to any rights of the Owner or Contractor under this Contract.

AIA Continuation G703

JobId: 830
STFD New Training Facility

Application no.: 4
Application date: 10/31/25
Period to: 10/31/25
Architect's project no.: 2507

A Item No.	B Description of Work	C Scheduled Value	D WORK COMPLETED		F Materials Presently Stored (not in D)	G		H Balance To Finish (Prev.)	I Retainage (Prev.)
			From Prev. Application	Amount This Period		Total Compl. and Stored To Date (D+F)	% Compl. (Prev.)		
1	Bond, Permit, Insurance, etc	15,194.28	15,194.28	0.00	0.00	15,194.28	100	0.00	1,519.43
2	Temporary Facilities and Controls	11,108.99	6,776.48	1,444.17	0.00	8,220.65	74	2,888.34	822.07
3	Anchor Bolts	1,159.60	1,159.60	0.00	0.00	1,159.60	100	0.00	115.96
4	Place and Finish Foundations -	30,948.65	30,948.65	0.00	0.00	30,948.65	100	0.00	3,094.87
5	Thermal Insulation	0.00	0.00	0.00	0.00	0.00	0	0.00	0.00
6	Doors, Frames and Hardware	23,821.20	15,017.00	0.00	0.00	15,017.00	63	8,804.20	1,501.70
7	Overhead Coiling Doors	8,565.99	0.00	8,565.99	0.00	8,565.99	100	0.00	856.60
8	Windows & Glazing	7,220.85	0.00	0.00	0.00	0.00	0	7,220.85	0.00
9	Metal Framing	20,174.77	20,174.77	0.00	0.00	20,174.77	100	0.00	2,017.48
10	Drywall	0.00	0.00	0.00	0.00	0.00	0	0.00	0.00
11	Accoustical Ceilings	19,033.73	0.00	0.00	0.00	0.00	0	19,033.73	0.00
12	Flooring	16,471.29	0.00	0.00	0.00	0.00	0	16,471.29	0.00
13	Painting & Coating, Accoustical, Framing	14,944.96	0.00	7,173.58	0.00	7,173.58	48	7,771.38	717.36
14	Toilet/Bath/Laundry Accessories	813.44	0.00	0.00	0.00	0.00	0	813.44	0.00
15	Fire Protection Specialties	699.21	633.00	0.00	0.00	633.00	91	66.21	63.30
16	Countertops & Cabinets	13,335.44	0.00	0.00	0.00	0.00	0	13,335.44	0.00
17	Metal Building Systems	92,884.21	92,884.21	0.00	0.00	92,884.21	100	0.00	9,288.42
18	Plumbing	39,380.12	31,504.10	0.00	0.00	31,504.10	80	7,876.02	3,150.41
19	HVAC	61,505.52	33,350.00	17,699.58	0.00	51,049.58	83	10,455.94	5,104.96
20	Electrical	52,182.14	22,438.32	7,200.00	4,300.00	33,938.32	65	18,243.82	3,393.83
Page Totals		429,444.39	270,080.41	42,083.32	4,300.00	316,463.73	74	112,980.66	31,646.39

AIA Continuation G703

JobId: 830
STFD New Training Facility

Application no.: 4
Application date: 10/31/25
Period to: 10/31/25
Architect's project no.: 2507

A Item No.	B Description of Work	C Scheduled Value	D		E	F Materials Presently Stored (not in D)	G		H Balance To Finish (Prev.)	I Retainage (Prev.)	
			WORK COMPLETED				Amount This Period	Total Compl. and Stored To Date (D+F)			% Compl. (Prev.)
			From Prev. Application								
21	Excavation & Fill	18,731.07	11,450.00		3,722.17	0.00	15,172.17	81	3,558.90	1,517.22	
22	Soil Treatment	113.07	113.07		0.00	0.00	113.07	100	0.00	11.31	
23	Concrete Paving	10,231.47	0.00		10,231.47	0.00	10,231.47	100	0.00	1,023.15	
		458,520.00	281,643.48		56,036.96	4,300.00	341,980.44	75	116,539.56	34,198.07	
