


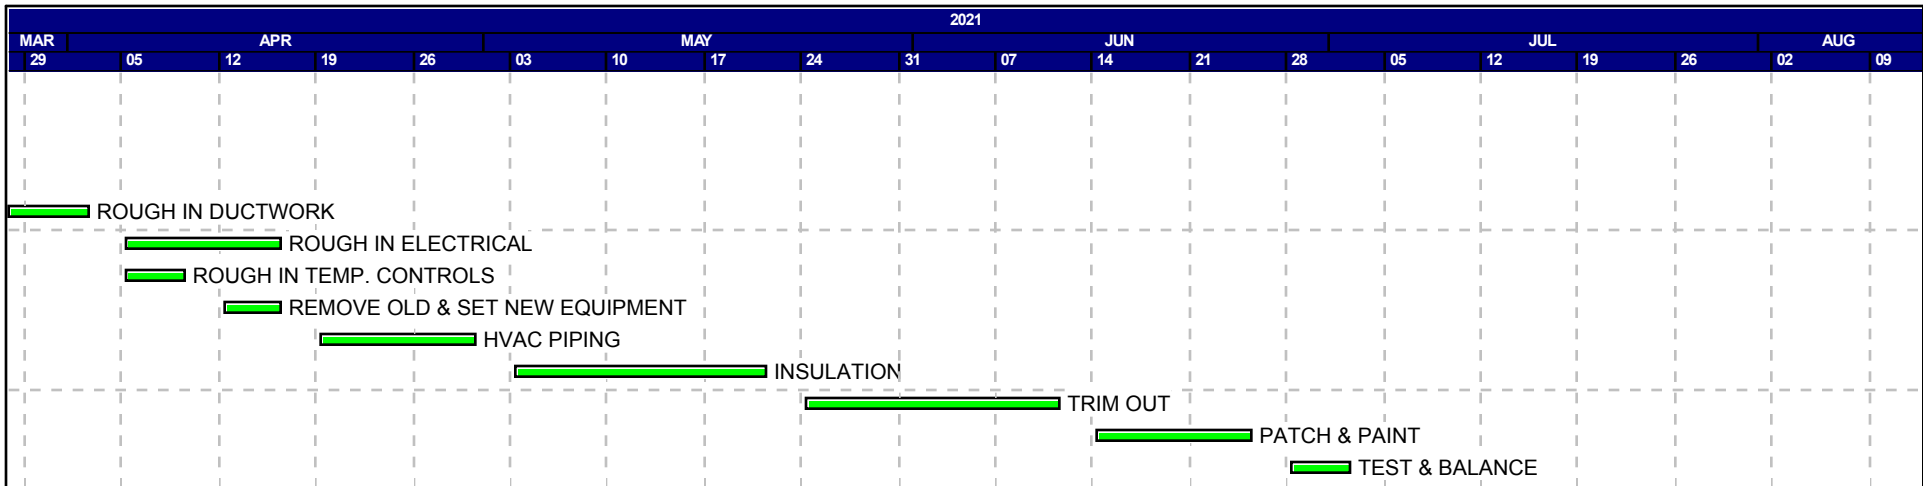
Act ID	Description	Orig Dur	Early Start	Early Finish	%	2021																
						JAN			FEB			MAR										
						18	25	01	08	15	22	01	08	15	22							
1000	MOBILIZATION	2d	25JAN21	26JAN21	0																	
1010	ASBESTOS ABATEMENT	3d	27JAN21	29JAN21	0																	
1020	CEILING REMOVAL	5d	01FEB21	05FEB21	0																	
1030	DEMOLITION	20d	08FEB21	05MAR21	0																	
1040	ROUGH IN DUCTWORK	20d	08MAR21	02APR21	0																	
1050	ROUGH IN ELECTRICAL	10d	05APR21	16APR21	0																	
1060	ROUGH IN TEMP. CONTROLS	5d	05APR21	09APR21	0																	
1070	REMOVE OLD & SET NEW EQUIPMENT	5d	12APR21	16APR21	0																	
1080	HVAC PIPING	10d	19APR21	30APR21	0																	
1090	INSULATION	15d	03MAY21	21MAY21	0																	
1100	TRIM OUT	15d	24MAY21	11JUN21	0																	
1110	PATCH & PAINT	10d	14JUN21	25JUN21	0																	
1120	TEST & BALANCE	5d	28JUN21	02JUL21	0																	



Start date	25JAN21
Finish date	02JUL21
Data date	25JAN21
Run date	21JAN21
Page number	1A
© Primavera Systems, Inc.	

**ARC MECHANICAL
TROOP L HVAC REPLACEMENT**

-  Early bar
-  Progress bar
-  Critical bar
-  Summary bar
-  Start milestone point
-  Finish milestone point



Start date	25JAN21
Finish date	02JUL21
Data date	25JAN21
Run date	21JAN21
Page number	1B
© Primavera Systems, Inc.	

ARC MECHANICAL TROOP L HVAC REPLACEMENT

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point
