



STJHS Termite Repair
Pre- Construction Meeting #1
3/12/2025
Agenda

- I. **Introduction**
 - a. Steele McDaniel –Project Manger
 - b. Zac Jourdan – Project Manager
 - c. James Harmon- Superintendent
 - d. See list of Subcontractors

- II. **Communication**
 - a. Zac Jourdan will be the point of contact for this project for SRD
 - b. _____ will be the point of contact for this project for STPSB
 - c. _____ will be the point of contact for this project for Architect

- III. **Contract**
 - a. Executed Contract Received

- IV. **Permits**
 - a. Pending
 - i. Full Set of Plans
 - ii. Completed Permit Application

- V. **Schedule**
 - a. Start date: March 25th – 120 Calendar Day Project
 - b. Schedule provided

- VI. **Site usage**
 - a. Parking location for workers:
 - b. Material lay down area or staging area:
 - c. Dumpster location:
 - d. Temp toilet location:

- VII. **Meetings**
 - a. Monthly meeting:
 - b. Location: Onsite

- VIII. **Monthly pay app**
 - a. Procore Generated pay app
 - b. Draft Submitted for approval at the end of month
 - c. Submit original after approval.



- i. How many copies:
- ii. Notarized:

IX. Submittals

- a. Submitted by: 3/19

X. Questions for Owner

- a. Storage for lockers
- b. Work schedule during testing



Steele-R Development
 120 Innwood Drive
 Covington, LA 70433

Date: 3/12/2025

SCHEDULE OF VALUES

Project No: PO514
 Project: STJHS Termite Damage Repair
 Contractor: Steele-R Development LLC

Proposal No: _____
 Project No: 867


ITEM NO.	DESCRIPTION	SCHEDULED VALUE
1	Bond	\$ 6,100.00
2	General Conditons	\$ 45,000.00
3	Moblization	\$ 5,000.00
4	Stucco	\$ 7,000.00
5	Structural Steel	\$ 45,000.00
6	Rough Carpentry Materials	\$ 6,500.00
7	Rough Carpentry Labor	\$ 10,000.00
8	Roofing	\$ 85,000.00
9	Access Doors	\$ 1,000.00
10	Drywall Labor	\$ 10,000.00
12	Drywall and Suspended Ceiling System Material	\$ 7,500.00
13	ACT Material	\$ 4,000.00
14	ACT Labor	\$ 2,000.00
15	Paint Material	\$ 6,500.00
15	Paint Labor	\$ 15,000.00
16	Sprinkler	\$ 20,000.00
16	Plumbing	\$ 2,000.00
18	HVAC	\$ 38,000.00
19	Electrical	\$ 32,000.00
Total		\$ 347,600.00

867 - St. Tammany Junior High School Termite Repair

Submittal Schedule

Section #	Submittal	Contractor/Subcontractor	Status
05-100	Structural Metals	Nagims Custome Welding and Fabrication	Returned 3/11
06-100	Rough Carpentry	Steele-R Development	Pending Submission by GC
07-200	Thermal Protection - Insuation	Steele-R Development	Pending Submission by GC
07-300	Shingles, Roof Tiles, and Roof Coverings	Ibos Roofing	Submitted 3/11
08-300	Speciality Doors	Steele-R Development	Pending Submission by GC
08-500	Windows	Northlake Glass	Pending Submission by GC
09-250	Gypsum Wallboard	Steele-R Development	Pending Submission by GC
09-800	Acoustical Treatment	Steele-R Development	Pending Submission by GC
09-810	Stucco	Steele-R Development	Pending Submission by GC
09-900	Paints and Coatings	Steele-R Development	Pending Submission by GC
13-900	Fire Suppression	Jefferson Sprinkler	Pending Submission by GC
15-100	Plumbing	Steele-R Development	Pending Submission by GC
15-700	HVAC	Loumis Air, LLC	Pending Submission by GC
16-100-2	Electrical Mounting Kits	Robin Services, Inc.	Pending Submission by GC
16-100-1	Electrical	Robin Services, Inc.	Pending Submission by GC

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	April 2025											
								8	11	14	17	20	23	26	29	1	4	7	
1	🚀	Electrical Testing	1 day	Mon 3/17/25	Mon 3/17/25														
2	🚀	HVAC Testing	1 day	Mon 3/17/25	Mon 3/17/25														
3	📅	NTP	1 day	Tue 3/25/25	Tue 3/25/25														
4	🚀	Moblize	1 day	Tue 3/25/25	Tue 3/25/25														
5	📅	Install Fence	1 day	Tue 3/25/25	Tue 3/25/25														
6	🚀	Set Dumpster	1 day	Tue 3/25/25	Tue 3/25/25														
7	🚀	Electrical Make Safe	2 days	Wed 3/26/25	Thu 3/27/25	3													
8	🚀	Remove/Store Elec Equipment to be reused	2 days	Fri 3/28/25	Mon 3/31/25	7													
9	🚀	Remove/Store smoke det/grilles, & registers	2 days	Fri 3/28/25	Mon 3/31/25	8SS													
10	🚀	Protect plumbing fixtures and pipes	2 days	Fri 3/28/25	Mon 3/31/25	9SS													
11	🚀	Remove and Store Lockers	5 days	Tue 4/1/25	Mon 4/7/25	9													
12	🚀	Temp Support Exter Conduit	2 days	Tue 4/8/25	Wed 4/9/25	11													
13	🚀	Temp Support FA and Speaker Ext	2 days	Tue 4/8/25	Wed 4/9/25	12SS													
14	🚀	Demo Ceilings	5 days	Thu 4/10/25	Wed 4/16/25	13													
15	🚀	Isloate Sprinkle System in work area	1 day	Thu 4/17/25	Thu 4/17/25	14													
16	🚀	Demo sprinkler line	1 day	Fri 4/18/25	Fri 4/18/25	15													
17	🚀	Demo Duct Work	2 days	Fri 4/18/25	Mon 4/21/25	15													
18	🚀	Demo and replace board trim	2 days	Fri 4/18/25	Mon 4/21/25	15													
19	🚀	Protect existing interior features to remain	1 day	Tue 4/22/25	Tue 4/22/25	17													
20	🚀	TESTING NO WORK	7 days	Wed 4/23/25	Thu 5/1/25	19													
21	🚀	Install Shoring	1 day	Fri 5/2/25	Fri 5/2/25	20													
22	🚀	Demo Wood Roof	5 days	Mon 5/5/25	Fri 5/9/25														
23	🚀	Demo Gutters and downspouts	5 days	Mon 5/5/25	Fri 5/9/25														
24	🚀	Install Temp protection from rain	1 day	Thu 5/15/25	Thu 5/15/25	22													
25	🚀	Reroute down spouts	2 days	Thu 5/15/25	Fri 5/16/25	23													
26	🚀	Anchor and set new HHS 4x4x1/4 Columns	5 days	Mon 5/19/25	Fri 5/23/25	25													
27	🚀	Set new W12X16 beams	5 days	Mon 5/26/25	Fri 5/30/25	26													
28	🚀	Install top Plates on Steel Beams	3 days	Mon 6/2/25	Wed 6/4/25	27													
29	🚀	Install 2x6 treated joists	3 days	Thu 6/5/25	Mon 6/9/25	28													
30	🚀	Frame for new knee wall	3 days	Tue 6/10/25	Thu 6/12/25	29													
31	🚀	Frame for new stud wall	2 days	Fri 6/13/25	Mon 6/16/25	30													
32	🚀	Install 5/8 Sheating & 1x6 Facia	4 days	Tue 6/10/25	Fri 6/13/25	29													
33	🚀	Install New Siplast Roof	8 days	Mon 6/16/25	Wed 6/25/25	32													
34	🚀	Install piping to new vent stacks	1 day	Thu 7/3/25	Thu 7/3/25	59													
35	🚀	6" unfaced batt isulation with poultry netting- in between wood joist	2 days	Thu 6/26/25	Fri 6/27/25	33													
36	🚀	HVAC Rough In	5 days	Thu 6/26/25	Wed 7/2/25	33													
37	🚀	Electrical Rough IN	2 days	Thu 6/26/25	Fri 6/27/25	33													

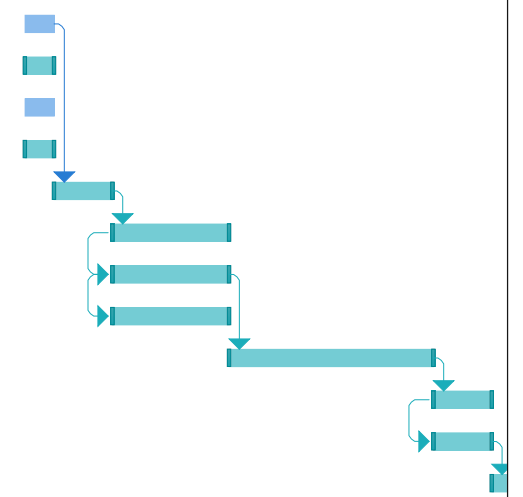

Project: 868 STJHS Termite Rep Date: Wed 3/12/25	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	April 2025														
								8	11	14	17	20	23	26	29	1	4	7				
38	🚀	Framing Inspection	1 day	Thu 7/3/25	Thu 7/3/25	36																
39	🚀	HVAC Rough In Inspection	1 day	Thu 7/3/25	Thu 7/3/25	36																
40	🚀	Electrical Rough In Inspection	1 day	Mon 6/30/25	Mon 6/30/25	37																
41	🚀	Stucco Work Int/Ext	3 days	Thu 7/3/25	Mon 7/7/25																	
42	🚀	Replace cracked glass	1 day	Tue 7/8/25	Tue 7/8/25	41																
43	🚀	ACT Ceiling Grid	3 days	Tue 7/8/25	Thu 7/10/25																	
44	🚀	Rehook up sprinkler	2 days	Tue 7/8/25	Wed 7/9/25																	
45	🚀	Install Lights	2 days	Fri 7/11/25	Mon 7/14/25																	
46	🚀	Electrical Final Inspection	1 day	Mon 7/14/25	Mon 7/14/25																	
47	🚀	HVAC Final Connect	2 days	Fri 7/11/25	Mon 7/14/25																	
48	🚀	HAVC T&B	2 days	Mon 7/14/25	Tue 7/15/25																	
49	🚀	HVAC Final Inspection	1 day	Tue 7/15/25	Tue 7/15/25	47																
50	🚀	Install drywall	3 days	Tue 7/15/25	Thu 7/17/25																	
51	🚀	Float and Finish Drywall	2 days	Wed 7/16/25	Thu 7/17/25																	
52	🚀	Drywall Ceiling System	4 days	Tue 7/15/25	Fri 7/18/25																	
53	🚀	Install Gyp Ceiling	3 days	Wed 7/16/25	Fri 7/18/25																	
54	🚀	Install Access Ceiling Doors	1 day	Mon 7/21/25	Mon 7/21/25																	
55	🚀	Install ACT Ceiling	3 days	Tue 7/15/25	Thu 7/17/25																	
56	🚀	Paint Gyp Ceiling	5 days	Wed 7/16/25	Tue 7/22/25																	
57	🚀	Paint Int/Ext	5 days	Wed 7/9/25	Tue 7/15/25																	
58	🚀	Install Gutters and Downspouts	4 days	Wed 7/9/25	Mon 7/14/25																	
59	🚀	Install Splash Blocks	1 day	Tue 7/15/25	Tue 7/15/25																	
60	🚀	Reinstall Lockers	3 days	Tue 7/15/25	Thu 7/17/25																	
61	🚀	Reinstall smoke det/grilles, & registers	2 days	Fri 7/18/25	Mon 7/21/25																	
62	🚀	Punch List	2 days	Mon 7/21/25	Tue 7/22/25																	
63	🚀	Building Final	1 day	Wed 7/23/25	Wed 7/23/25																	

Project: 868 STJHS Termite Rep
Date: Wed 3/12/25

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
