


ID	Task Name	Duration	Start	Finish	Pred	Dec 11 '05	Dec 18 '05	Dec 25 '05	Jan 1 '06	Jan 8 '06	Jan 15 '06	Jan 22 '06	Jan 29 '06	Feb 5 '06	Feb 12 '06	Feb 19 '06	Feb 26 '06	Mar 5 '06	Mar 12 '06	Mar 19 '06	Mar 26 '06	Apr 2 '06	Apr 9 '06			
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	KENNER Med Ctr	0 days	Wed 1/11/06	Wed 1/11/06																						
2	PRIORITIES	0 days	Wed 3/8/06	Wed 3/8/06																						
3																										
4	ICU	43 days	Wed 1/11/06	Tue 3/7/06																						
5	Hospital fix AHU and Envelope	14 days	Wed 1/11/06	Sat 1/28/06																						
6	Complete Remediation	7 days	Sat 1/28/06	Tue 2/7/06	5																					
7	Viable Air Sampling	13 days	Tue 2/7/06	Thu 2/23/06	6																					
8	Buildback	9 days	Thu 2/23/06	Tue 3/7/06	7																					
9																										
10	Cath Lab	23.7 days	Sat 1/7/06	Tue 2/7/06																						
11	Complete Assessment	5 days	Sat 1/7/06	Fri 1/13/06																						
12	Complete Remediation	2 days	Sat 1/14/06	Tue 1/17/06																						
13	Viable Air Sampling	12 days	Mon 1/16/06	Tue 1/31/06																						
14	Buildback	12 days	Mon 1/23/06	Tue 2/7/06																						
15																										
16	Trauma 1&2	4 days	Tue 1/17/06	Sat 1/21/06																						
17	Flooring Issues	4 days	Tue 1/17/06	Sat 1/21/06																						
18																										
19	Trauma X Ray Room 12	46 days	Wed 1/11/06	Sat 3/11/06																						
20	Hospital Decide on Equipment	5 days	Wed 1/11/06	Tue 1/17/06																						
21	Address Shield Plan	5 days	Tue 1/17/06	Tue 1/24/06	20																					
22	CUT CER	2 days	Tue 1/24/06	Thu 1/26/06	21																					
23	Hospital determine Buildout	3 days	Thu 1/26/06	Mon 1/30/06	22																					
24	Complete Remediation	7 days	Mon 1/30/06	Wed 2/8/06	23																					
25	Non Viable Air Sampling	2 days	Wed 2/8/06	Fri 2/10/06	24																					
26	Buildback	22 days	Fri 2/10/06	Sat 3/11/06	25																					
27																										
28	FIRST FLOOR	0 days	Fri 3/31/06	Fri 3/31/06																						
29																										
30	CORRIDORS	0 days	Tue 2/14/06	Tue 2/14/06																						
31	Respiratory Therapy North Side	10 days	Fri 1/20/06	Thu 2/2/06																						
32	Containment and Remediation	3 days	Fri 1/20/06	Tue 1/24/06																						
33	Non-Viable Air Sampling	2 days	Tue 1/24/06	Thu 1/26/06	32																					
34	Buildback	5 days	Thu 1/26/06	Thu 2/2/06	33																					
35																										
36	Respiratory Therapy South Side	10 days	Wed 2/1/06	Tue 2/14/06																						
37	Containment and Remediation	3 days	Wed 2/1/06	Sat 2/4/06																						
38	Non-Viable Air Sampling	2 days	Sat 2/4/06	Tue 2/7/06	37																					
39	Buildback	5 days	Tue 2/7/06	Tue 2/14/06	38																					
40																										
41	MOB Connector North	11.3 days	Wed 1/18/06	Wed 2/1/06																						
42	Containment and Remediation	3 days	Wed 1/18/06	Sat 1/21/06																						
43	Non-Viable Air Sampling	2 days	Mon 1/23/06	Wed 1/25/06	42																					
44	Buildback	5 days	Thu 1/26/06	Wed 2/1/06	43																					
45																										
46	MOB Connector South	11 days	Wed 2/1/06	Wed 2/15/06																						
47	Containment and Remediation	4 days	Wed 2/1/06	Tue 2/7/06	44																					
48	Non-Viable Air Sampling	2 days	Tue 2/7/06	Thu 2/9/06	47																					
49	Buildback	5 days	Thu 2/9/06	Wed 2/15/06	48																					
50																										
51	West Corridor at A Elevators	10.4 days	Thu 1/19/06	Wed 2/1/06																						
52	Containment and Remediation	3 days	Thu 1/19/06	Mon 1/23/06																						
53	Non-Viable Air Sampling	2 days	Mon 1/23/06	Wed 1/25/06	52																					
54	Buildback	5 days	Thu 1/26/06	Wed 2/1/06	53																					
55																										
56	East Corridor at A Elevators	10 days	Wed 2/1/06	Tue 2/14/06																						
57	Containment and Remediation	3 days	Wed 2/1/06	Sat 2/4/06																						
58	Non-Viable Air Sampling	2 days	Sat 2/4/06	Tue 2/7/06	57																					
59	Buildback	5 days	Tue 2/7/06	Tue 2/14/06	58																					
60																										

Project: Kenner Homestretch
Date: Sun 1/22/06

Task: Progress Summary External Tasks Deadline

Split: Milestone: Project Summary: External Milestone:


Page 1

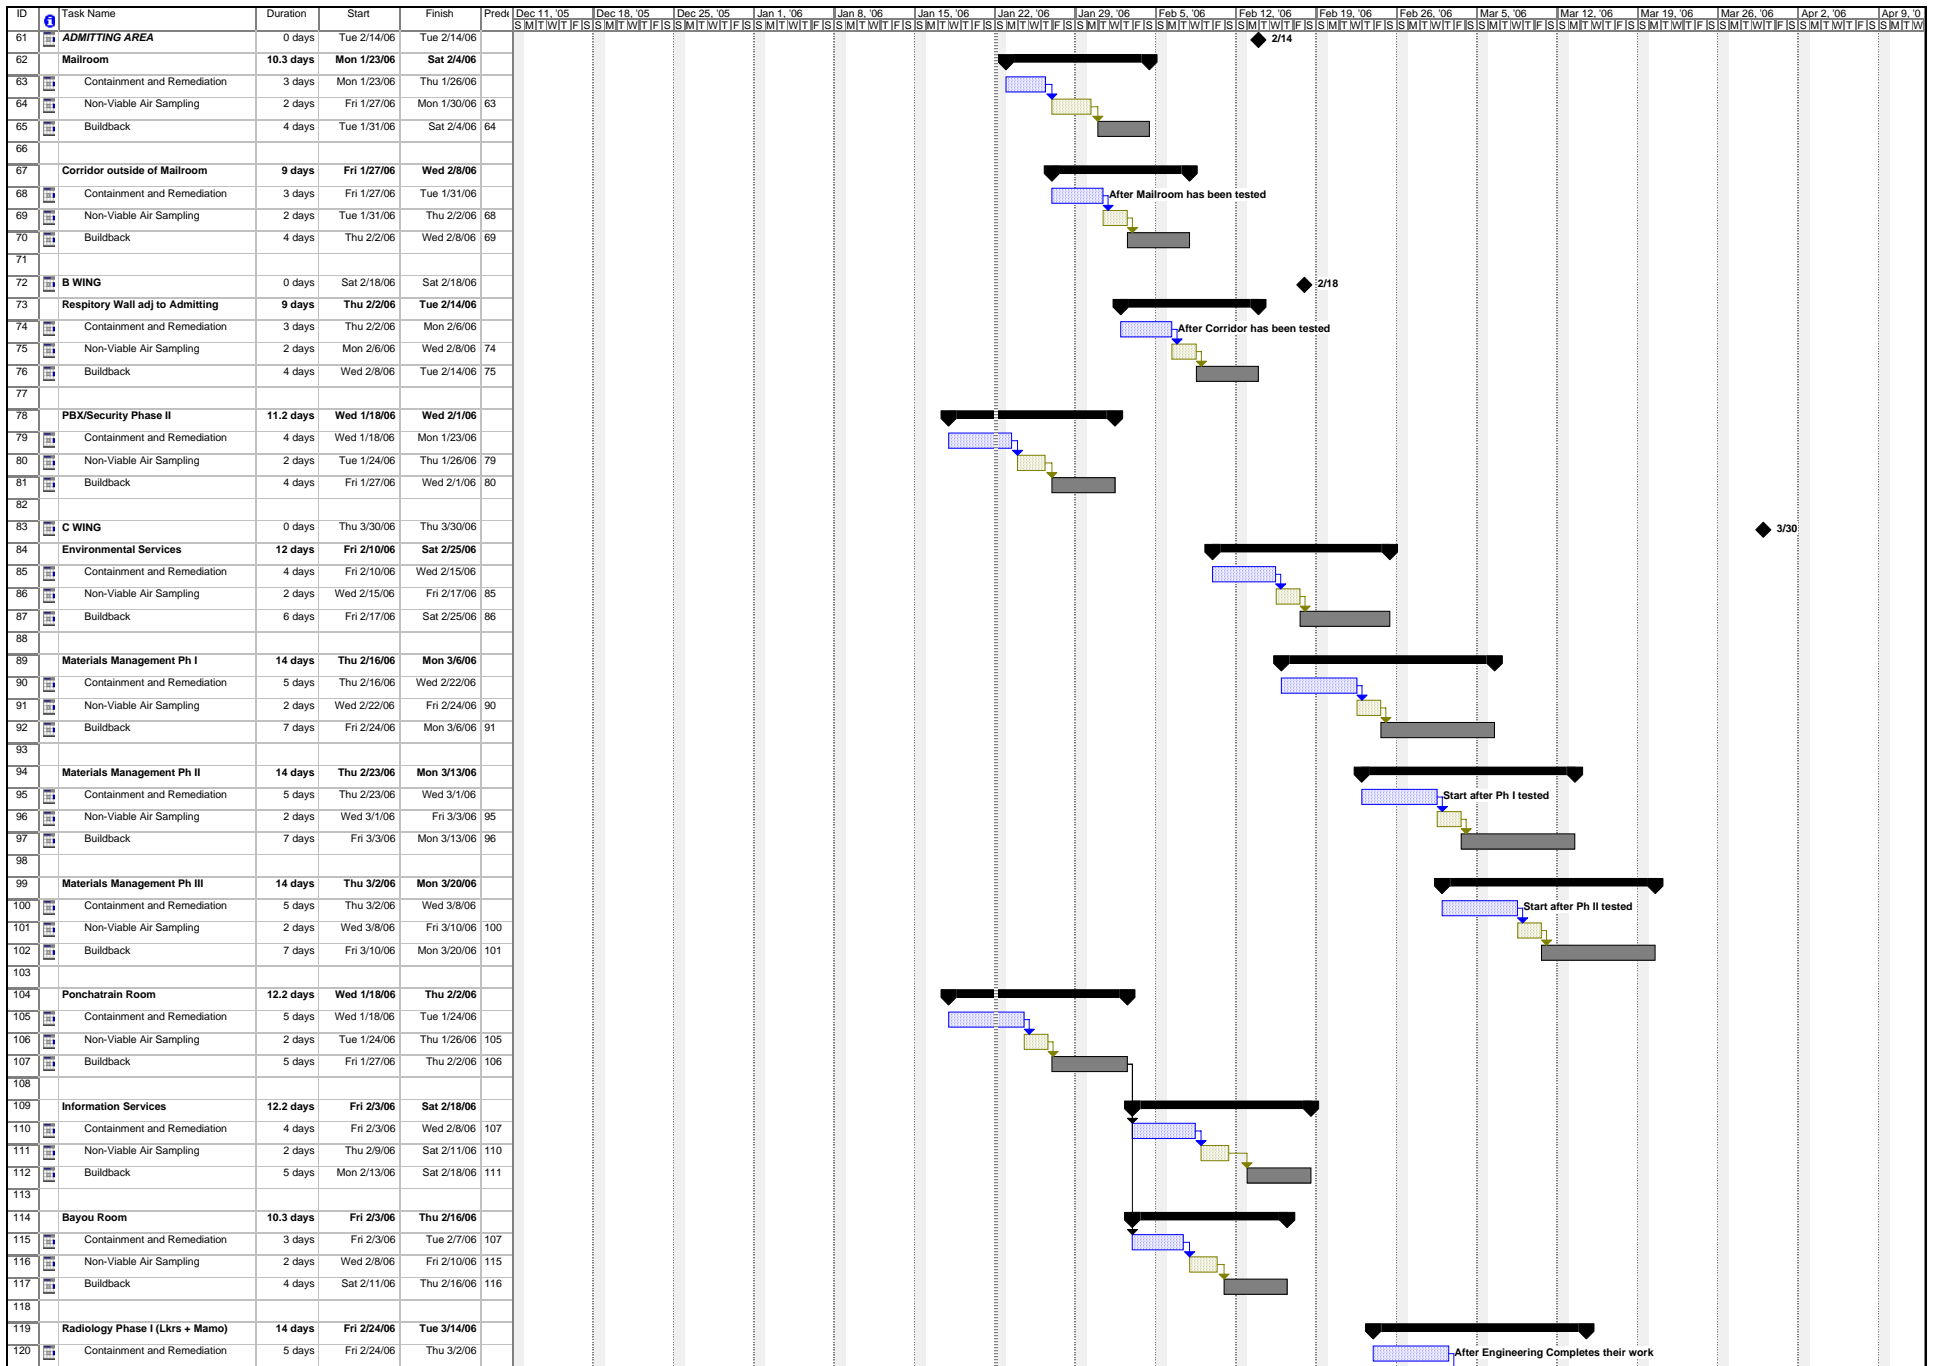

Project: Kenner Homestretch
Date: Sun 1/22/06

Task: Progress Summary External Tasks Deadline Split Milestone Project Summary External Milestone

Page 2

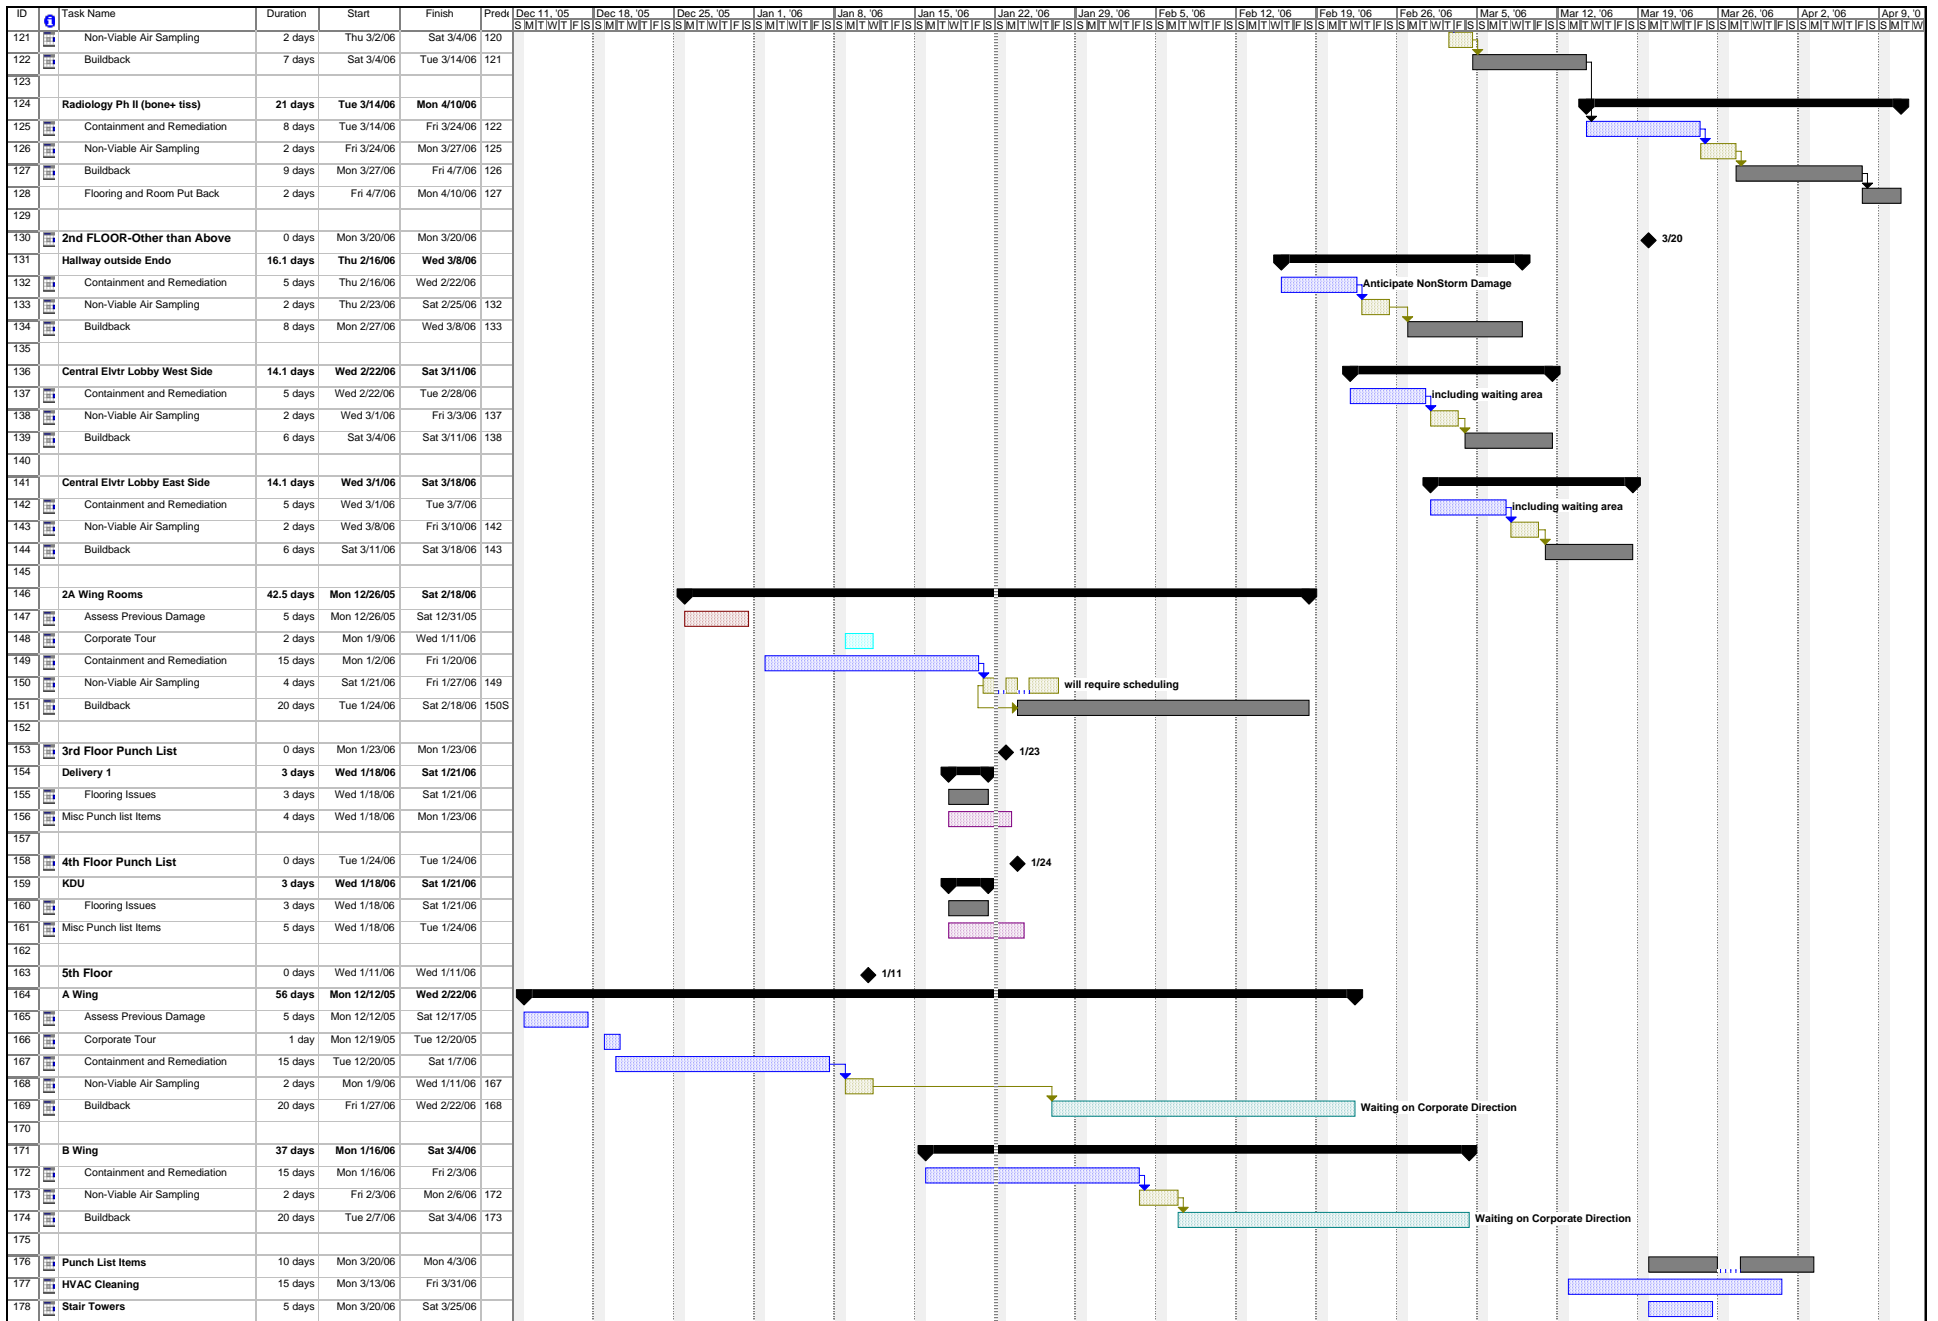

Project: Kenner Homestretch
Date: Sun 1/22/06

Task Split: Progress: Milestone:

Summary: Project Summary:

External Tasks: External Milestone:

Deadline:

Page 3
