ID	Task Name	Duration	Start	Finish
1	***KENNER MOB***	0 days	Sat 4/1/06	Sat 4/1/06
2				
3				
4	**Suite 103 Uribe**	**14 days**	**Sat 1/7/06**	**Tue 1/24/06**
5	Remediation	2 days	Sat 1/7/06	Tue 1/10/06
6	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
7	Buildback	4 days	Sat 1/14/06	Tue 1/24/06
8				
9	**Suite 205 Mcaine**	**13 days**	**Sat 1/7/06**	**Mon 1/23/06**
10	Remediation	2 days	Sat 1/7/06	Tue 1/10/06
11	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
12	Buildback	3 days	Sat 1/14/06	Mon 1/23/06
13				
14	**Suite 202 Sleep Lab**	**18 days**	**Sat 1/7/06**	**Sat 1/28/06**
15	Remediation	2 days	Sat 1/7/06	Tue 1/10/06
16	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
17	Buildback	8 days	Sat 1/14/06	Sat 1/28/06
18				
19	**Suite 210 Dr Fine**	**22 days**	**Sat 12/31/05**	**Thu 1/26/06**
20	Remediation	4 days	Sat 12/31/05	Tue 1/10/06
21	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
22	Buildback	10 days	Sat 1/14/06	Thu 1/26/06
23				
24	**Suite 104 DeBellevue**	**20 days**	**Sat 1/14/06**	**Tue 2/7/06**
25	Remediation	5 days	Sat 1/14/06	Tue 1/24/06
26	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
27	Buildback	4 days	Sat 1/28/06	Tue 2/7/06
28				
29	**Suite 105 Amulet**	**25.2 days**	**Sat 1/14/06**	**Mon 2/13/06**
30	Remediation	4 days	Sat 1/14/06	Tue 1/24/06
31	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
32	Buildback	6 days	Sat 1/28/06	Mon 2/13/06
33				
34	**Suite 106 Simion**	**14 days**	**Sat 1/14/06**	**Tue 1/31/06**
35	Remediation	3 days	Sat 1/14/06	Tue 1/24/06
36	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
37	Buildback	4 days	Sat 1/21/06	Tue 1/31/06
38				
39	**Suite 108 Cardio**	**26 days**	**Sat 1/7/06**	**Tue 2/7/06**
40	Remediation	4 days	Sat 1/7/06	Mon 1/16/06
41	Clearance Testing	2 days	Mon 1/16/06	Wed 1/18/06
42	Buildback	5 days	Sat 1/21/06	Tue 2/7/06
43				
44	**Suite T1018 Dialysis**	**20.1 days**	**Sat 1/21/06**	**Tue 2/14/06**
45	Remediation	4 days	Sat 1/21/06	Wed 2/1/06
46	Clearance Testing	2 days	Tue 1/31/06	Thu 2/2/06
47	Buildback	4 days	Sat 2/4/06	Tue 2/14/06
48				
49	**Suite 408**	**8.1 days**	**Fri 1/13/06**	**Mon 1/23/06**
50	Remediation	2 days	Fri 1/13/06	Mon 1/16/06
51	Clearance Testing	2 days	Mon 1/16/06	Wed 1/18/06
52	Buildback	4 days	Wed 1/18/06	Mon 1/23/06
53				
54	**Family Practice Conf Room**	**16 days**	**Sat 1/28/06**	**Thu 2/16/06**
55	Remediation	7 days	Sat 1/28/06	Mon 2/6/06
56	Clearance Testing	2 days	Mon 2/6/06	Wed 2/8/06
57	Buildback	7 days	Wed 2/8/06	Thu 2/16/06
58				
59	**Suite 409 Ph I**	**15 days**	**Fri 1/6/06**	**Tue 1/24/06**
60	Remediation	5 days	Fri 1/6/06	Tue 1/17/06
61	Clearance Testing	2 days	Tue 1/17/06	Thu 1/19/06
62	Buildback	3 days	Fri 1/20/06	Tue 1/24/06
63				
64	**Suite 409 Ph II**	**15 days**	**Fri 1/20/06**	**Tue 2/7/06**
65	Remediation	3 days	Fri 1/20/06	Tue 1/24/06
66	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
67	Buildback	6 days	Fri 1/27/06	Tue 2/7/06
68				
69	**Suite 412**	**20 days**	**Sat 1/28/06**	**Tue 2/21/06**
70	Remediation	3 days	Sat 1/28/06	Mon 2/6/06
71	Clearance Testing	2 days	Mon 2/6/06	Wed 2/8/06
72	Buildback	6 days	Sat 2/11/06	Tue 2/21/06
73				
74	**Suite 700**	**28 days**	**Fri 2/10/06**	**Wed 3/15/06**
75	Remediation	6 days	Fri 2/10/06	Wed 2/22/06
76	Clearance Testing	2 days	Wed 2/22/06	Fri 2/24/06
77	Buildback	8 days	Sat 2/25/06	Wed 3/15/06
78				
79	**Suite 701 Ph III Dr Z**	**21 days**	**Fri 2/10/06**	**Tue 3/7/06**
80	Remediation	3 days	Fri 2/10/06	Tue 2/14/06
81	Clearance Testing	2 days	Tue 2/14/06	Thu 2/16/06
82	Buildback	6 days	Sat 2/18/06	Tue 3/7/06
83				
84	**Suite PHN - 6**	**41 days**	**Fri 2/10/06**	**Thu 3/30/06**
85	Remediation	9 days	Fri 2/10/06	Wed 3/15/06
86	Clearance Testing	6 days	Mon 2/13/06	Fri 3/17/06
87	Buildback	15 days	Fri 2/17/06	Thu 3/30/06

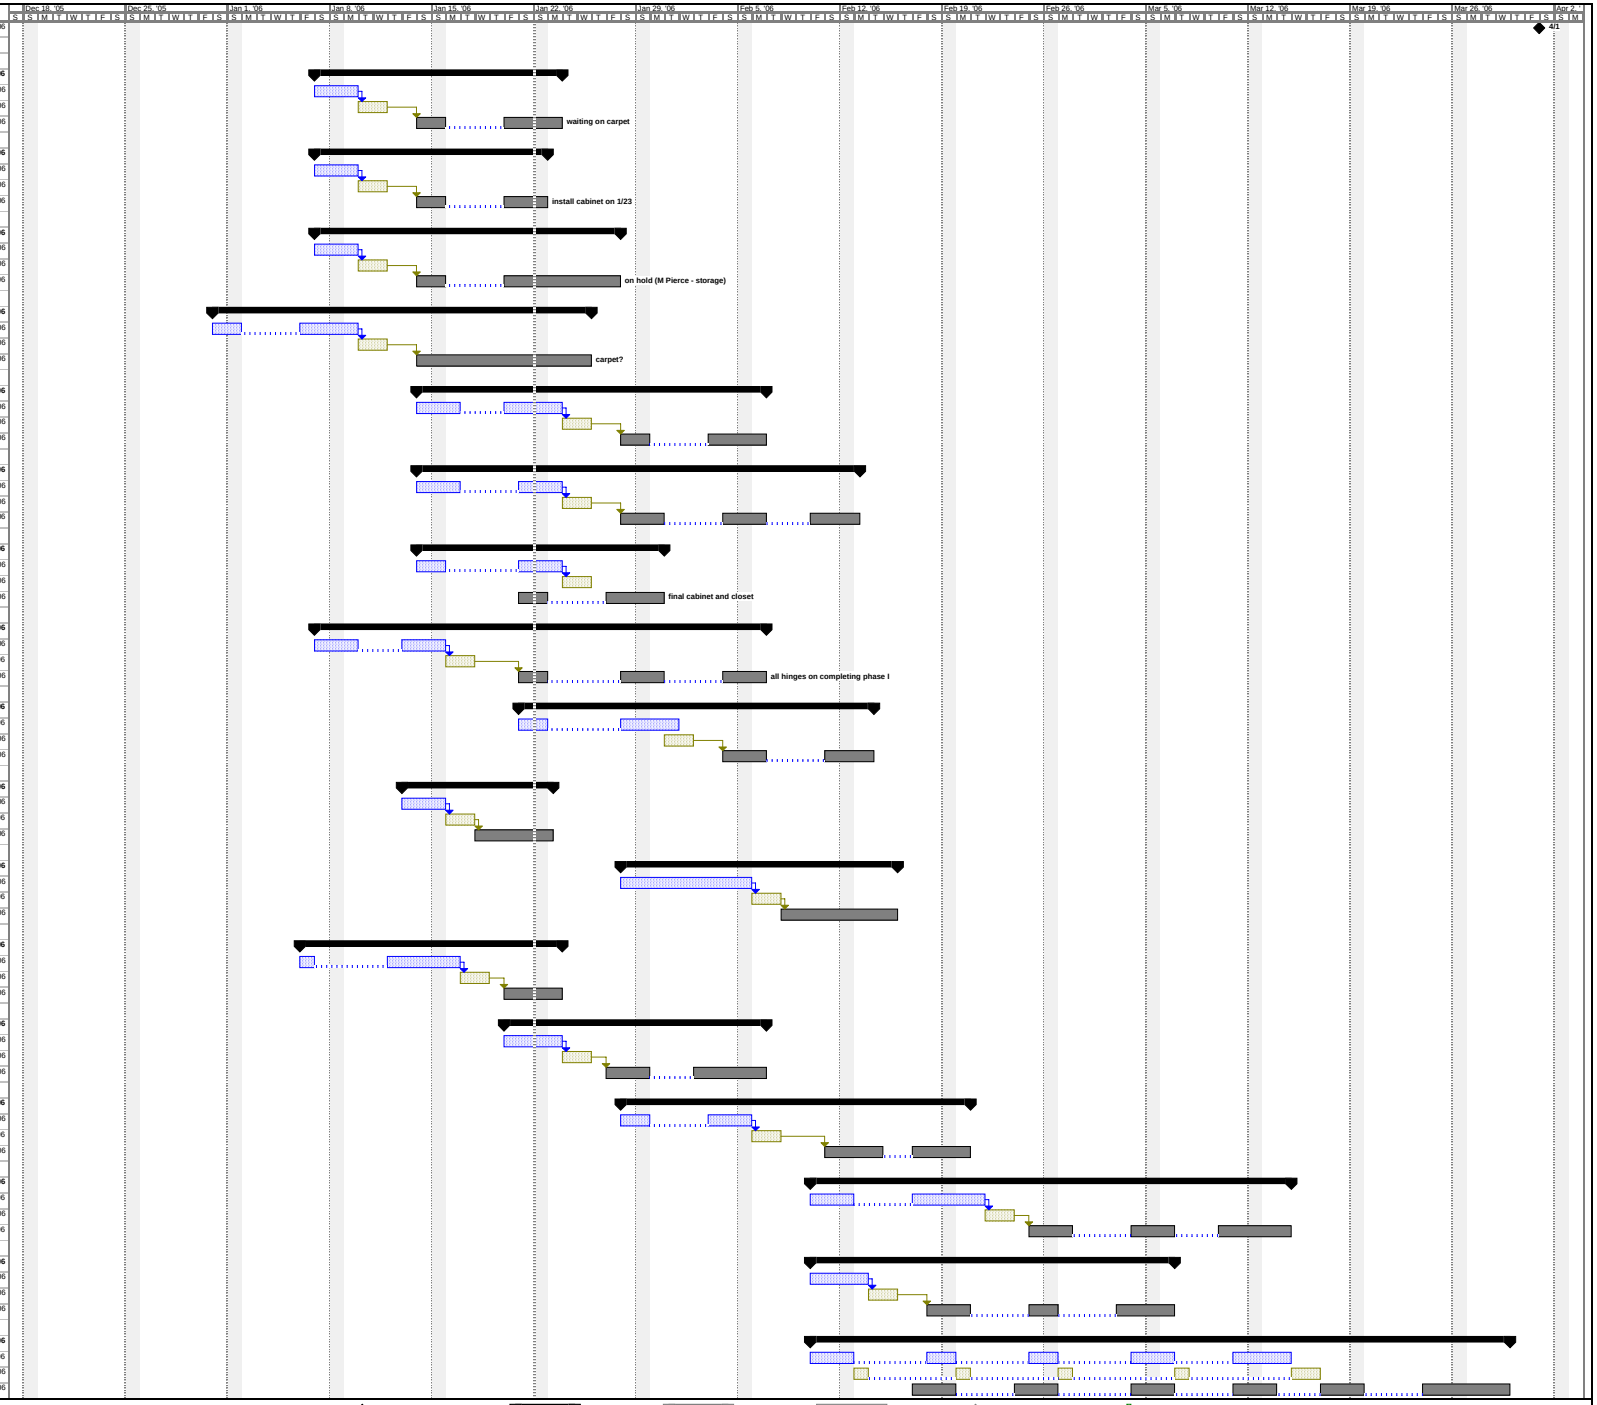

Project: KennerMOB Homestretch
Date: Sun 1/22/06

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
