ID	Task Name	Duration	Start	Finish
1	KENNER MOB	0 days	Sat 4/1/06	Sat 4/1/06
2				
3				
4	Suite 103 Uribe	14 days	Sat 1/7/06	Tue 1/24/06
5	Remediation	2 days	Sat 1/7/06	Tue 1/10/06
6	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
7	Buildback	4 days	Sat 1/14/06	Tue 1/24/06
8				
9	Suite 205 Mcaine	13 days	Sat 1/7/06	Mon 1/23/06
10	Remediation	2 days	Sat 1/7/06	Tue 1/10/06
11	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
12	Buildback	3 days	Sat 1/14/06	Mon 1/23/06
13				
14	Suite 202 Sleep Lab	18 days	Sat 1/7/06	Sat 1/28/06
15	Remediation	2 days	Sat 1/7/06	Tue 1/10/06
16	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
17	Buildback	8 days	Sat 1/14/06	Sat 1/28/06
18				
19	Suite 210 Dr Fine	22 days	Sat 12/31/05	Thu 1/26/06
20	Remediation	4 days	Sat 12/31/05	Tue 1/10/06
21	Clearance Testing	2 days	Tue 1/10/06	Thu 1/12/06
22	Buildback	10 days	Sat 1/14/06	Thu 1/26/06
23				
24	Suite 104 DeBellevue	20 days	Sat 1/14/06	Tue 2/7/06
25	Remediation	5 days	Sat 1/14/06	Tue 1/24/06
26	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
27	Buildback	4 days	Sat 1/28/06	Tue 2/7/06
28				
29	Suite 105 Amulet	25.2 days	Sat 1/14/06	Mon 2/13/06
30	Remediation	4 days	Sat 1/14/06	Tue 1/24/06
31	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
32	Buildback	6 days	Sat 1/28/06	Mon 2/13/06
33				
34	Suite 106 Simion	14 days	Sat 1/14/06	Tue 1/31/06
35	Remediation	3 days	Sat 1/14/06	Tue 1/24/06
36	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
37	Buildback	4 days	Sat 1/21/06	Tue 1/31/06
38				
39	Suite 108 Cardio	26 days	Sat 1/7/06	Tue 2/7/06
40	Remediation	4 days	Sat 1/7/06	Mon 1/16/06
41	Clearance Testing	2 days	Mon 1/16/06	Wed 1/18/06
42	Buildback	6 days	Sat 1/21/06	Tue 2/7/06
43				
44	Suite T1010 Dialysis	20.1 days	Sat 1/21/06	Tue 2/14/06
45	Remediation	4 days	Sat 1/21/06	Wed 2/1/06
46	Clearance Testing	2 days	Tue 1/31/06	Thu 2/2/06
47	Buildback	4 days	Sat 2/4/06	Tue 2/14/06
48				
49	Suite 408	8.1 days	Fri 1/13/06	Mon 1/23/06
50	Remediation	2 days	Fri 1/13/06	Mon 1/16/06
51	Clearance Testing	2 days	Mon 1/16/06	Wed 1/18/06
52	Buildback	4 days	Wed 1/18/06	Mon 1/23/06
53				
54	Family Practice Conf Room	16 days	Sat 1/28/06	Thu 2/16/06
55	Remediation	7 days	Sat 1/28/06	Mon 2/6/06
56	Clearance Testing	2 days	Mon 2/6/06	Wed 2/8/06
57	Buildback	7 days	Wed 2/8/06	Thu 2/16/06
58				
59	Suite 400 Ph I	15 days	Fri 1/6/06	Tue 1/24/06
60	Remediation	5 days	Fri 1/6/06	Tue 1/17/06
61	Clearance Testing	2 days	Tue 1/17/06	Thu 1/19/06
62	Buildback	3 days	Fri 1/20/06	Tue 1/24/06
63				
64	Suite 400 Ph II	15 days	Fri 1/20/06	Tue 2/7/06
65	Remediation	3 days	Fri 1/20/06	Tue 1/24/06
66	Clearance Testing	2 days	Tue 1/24/06	Thu 1/26/06
67	Buildback	6 days	Fri 1/27/06	Tue 2/7/06
68				
69	Suite 412	20 days	Sat 1/28/06	Tue 2/21/06
70	Remediation	3 days	Sat 1/28/06	Mon 2/6/06
71	Clearance Testing	2 days	Mon 2/6/06	Wed 2/8/06
72	Buildback	6 days	Sat 2/11/06	Tue 2/21/06
73				
74	Suite 700	26 days	Fri 2/10/06	Wed 3/15/06
75	Remediation	6 days	Fri 2/10/06	Wed 2/22/06
76	Clearance Testing	2 days	Wed 2/22/06	Fri 2/24/06
77	Buildback	8 days	Sat 2/25/06	Wed 3/15/06
78				
79	Suite 701 Ph III Pt 2	21 days	Fri 2/10/06	Tue 3/7/06
80	Remediation	3 days	Fri 2/10/06	Tue 2/14/06
81	Clearance Testing	2 days	Tue 2/14/06	Thu 2/16/06
82	Buildback	6 days	Sat 2/18/06	Tue 3/7/06
83				
84	Suite PHII - 6	41 days	Fri 2/10/06	Thu 3/30/06
85	Remediation	9 days	Fri 2/10/06	Wed 3/15/06
86	Clearance Testing	6 days	Mon 2/13/06	Fri 3/17/06
87	Buildback	15 days	Fri 3/17/06	Thu 3/30/06

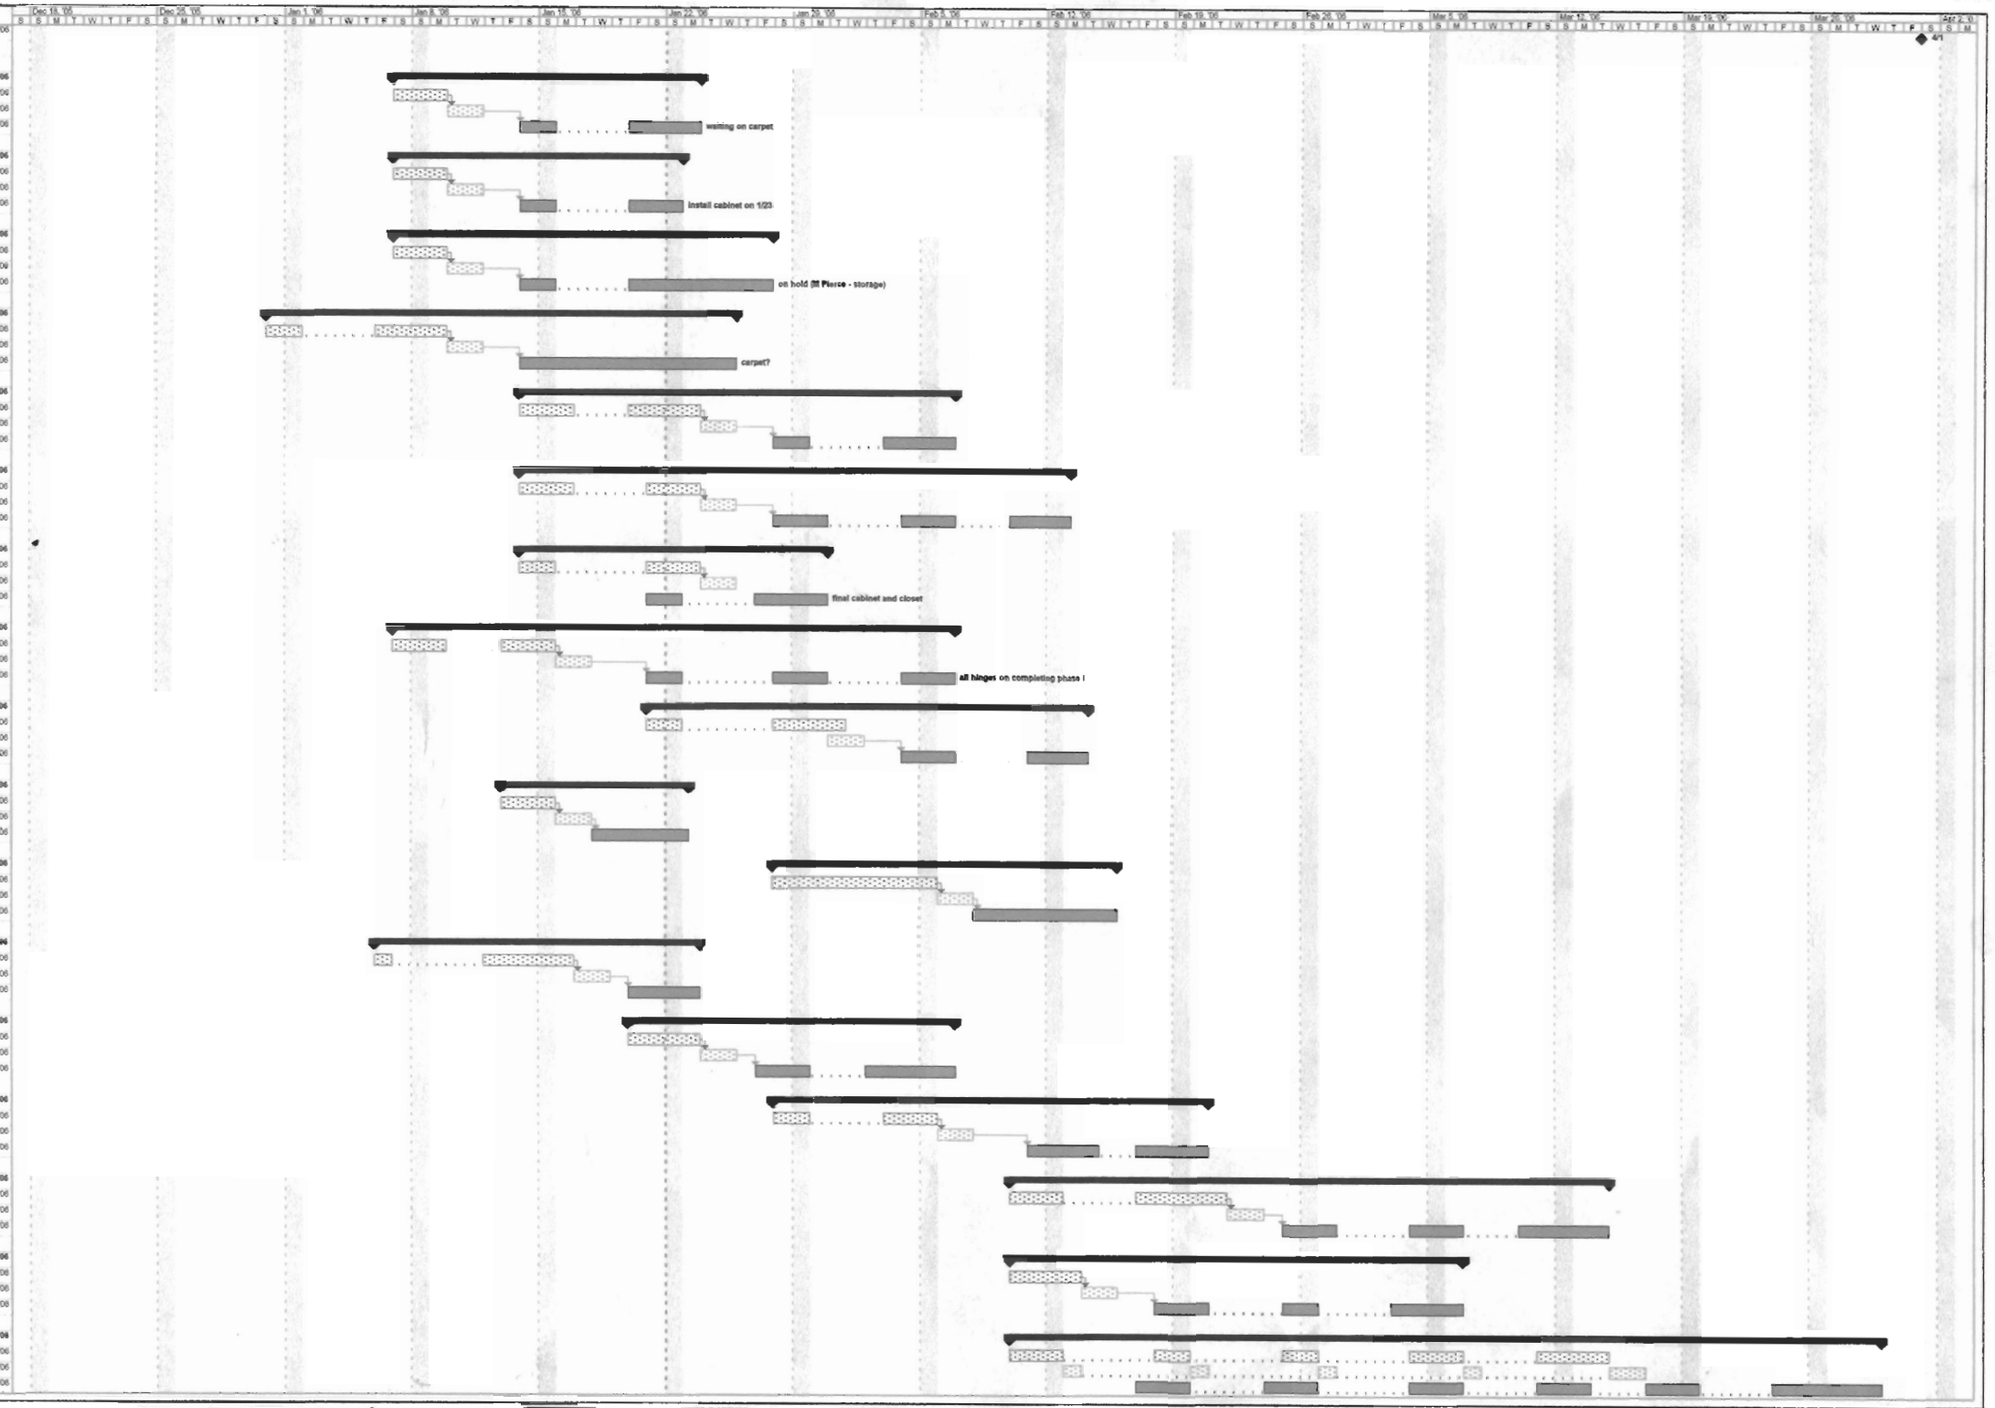

Project: KennerMOB Homestretch
Date: Sun 1/22/06

Task | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
